

FIELD REPORT

PROJECT: Leavelle McCampbell Middle **FIELD REPORT NO.:** Forty (40)

CONTRACT: Construction Management @ Risk **ARCHITECTS**
HG Reynolds **PROJECT NO.:**

DISTRIBUTION: **Owner:** Dr. Shawn Foster, Aiken County Schools
Mr. Kevin Chipman, Aiken County Schools
Ms. Michelle Padgett, Aiken County Schools
Ms. Beth Clark, Aiken County Schools
Mr. Kip Gunter, Aiken County Schools
Ms. Sandra Waddell, Aiken County Schools
Mr. Jeremiah Jones, Aiken County Schools

Architect: Mr. Donnie Love, McMillan Pazdan Smith
Mr. Bill Williams, WCI
Mr. Robert Wayne, WCI

Consultant: Mr. Mayhar Angooraj, BGA
Mr. William Wafer, BGA
Mr. Dan Reider, BGA

Contractor: Mr. Tilden Hilderbrand, Hass & Hilderbrand
Mr. Jeffrey Reynolds, HG Reynolds
Mr. Robert Lowe, HG Reynolds
Mr. Graham Reynolds, HG Reynolds

1) The Contractor (Electrical) continues rough-in is approximately 100 % percent first floor. As second floor rough in and is consistent with contracted scope of work.

DATE: July 7, 2016 **WEATHER:** Hot / 98 / Sunshine

TIME: 10:00 am **SCHEDULE** On Schedule

COMMENTS:

PRESENT AT SITE:

General Contractors, HVAC, plumbing, electrical, masonry.

OBSERVATION:

- 2) The Contractor (Masonry) is continuous approximately (75%) percent.
- 3) CMU point up work is ongoing as clean up continues.
- 4) Contractor install of joists and welding is consistent with required welding as observe and inspected by CSRA @ first floor over cafeteria and mechanical room.
- 5) The Contractor (HVAC) continues hanging duct and make-up of duct nearing completion as WCI coordinates CCI inspections as required and logged (100 %) percent first floor. Second floor rough in and is consistent with contracted scope of work.
- 6) Contractor site maintenance and cleanup is continuous with current CMU grout debris.
- 7) Above slab plumbing is progressing as riser installation is nearing (100%) percent.

SUBMITTALS:

- 1) Submission is in progress.

COORDINATION:

- 1) Bi-weekly meeting Tuesday 10:00 am, July 12, 2016. Offsite at Gold Mech offices

McMILLAN PAZDAN SMITH


FIELD REPORT

WCI GROUP LLC

FIELD REPORT

PROJECT: Leavelle McCampbell Middle **FIELD REPORT NO.:** Forty (40)

CONTRACT: Construction Management @ Risk **ARCHITECTS**
HG Reynolds **PROJECT NO.:**

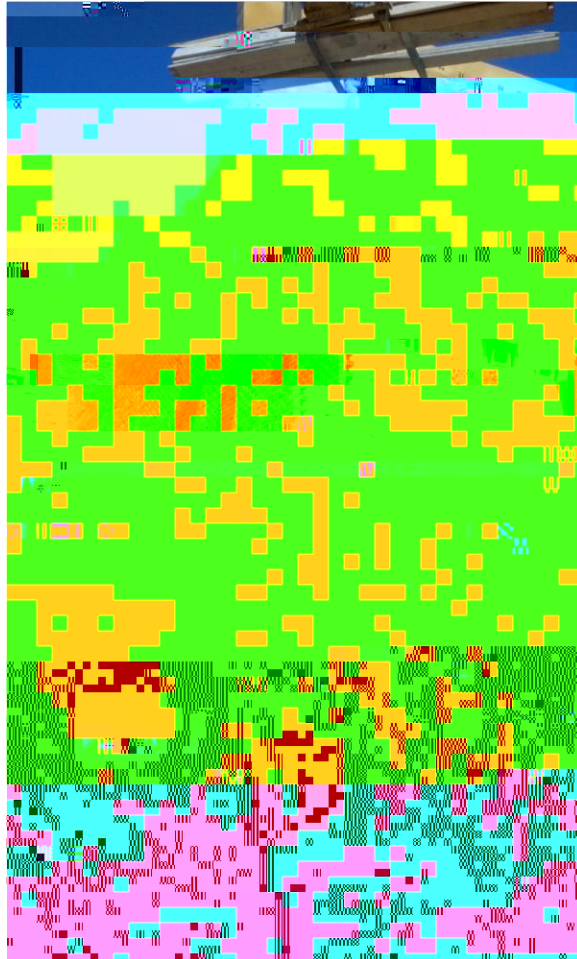

Masonry Veneer is approximately (75%) percent overall

FIELD REPORT

PROJECT: Leavelle McCampbell Middle **FIELD REPORT NO.:** Forty (40)

CONTRACT: Construction Management @ Risk **ARCHITECTS**
HG Reynolds **PROJECT NO.:**



Masonry construction is consistent and aggressive

Report By: R. Wayne Jr. / WCI Group
